

Langhorne-Yardley Road Intersection Improvements Middletown Township, Bucks County, PA SR 2049 Section BLW MPMS No. 107794

Middletown Township Board of Supervisors Meeting Monday, July 20, 2020












Project Overview Plan

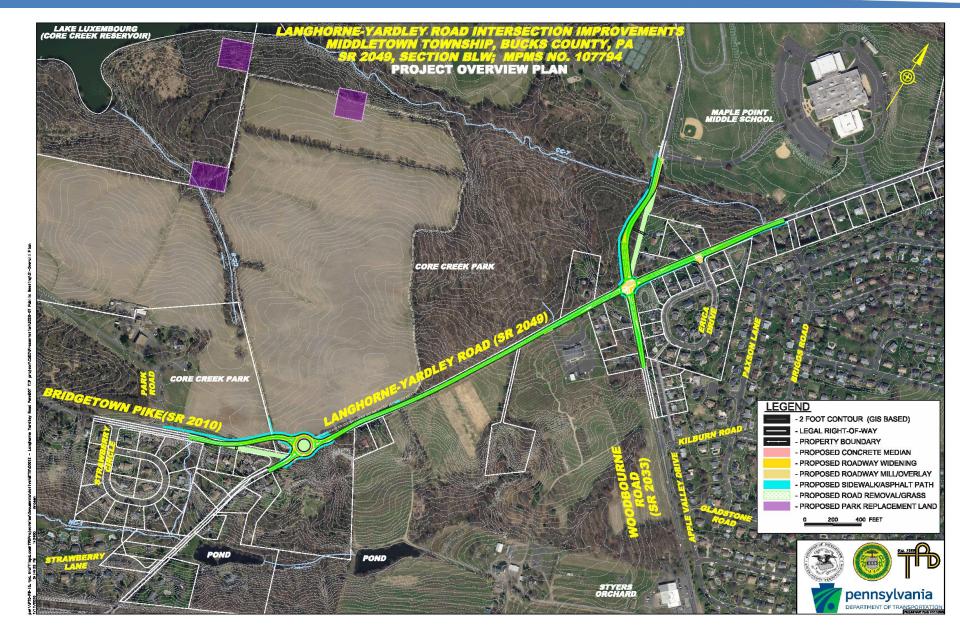

Roundabout

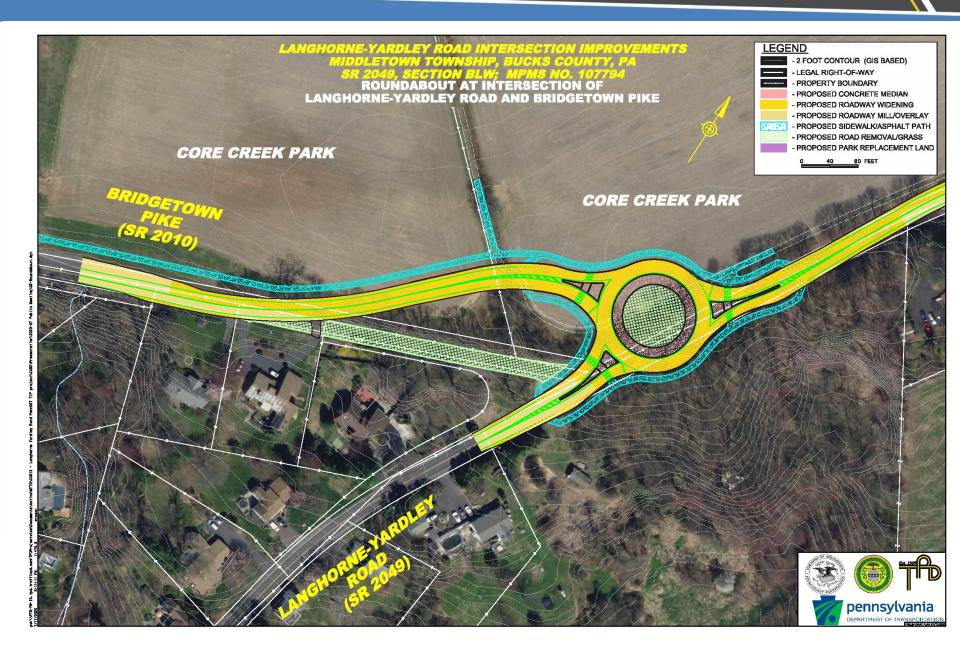

Woodbourne Road Realignment

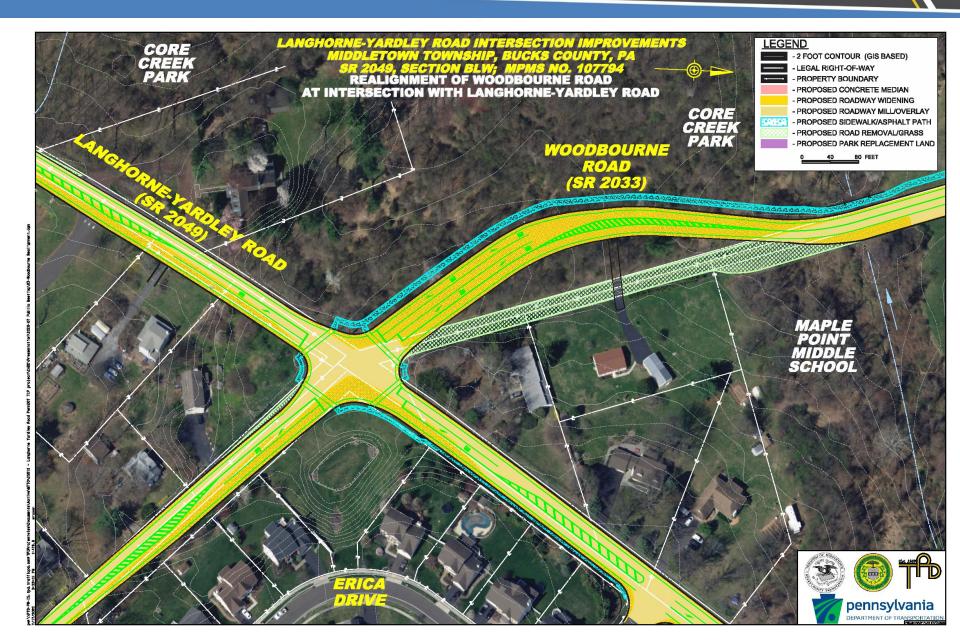

Improvement Highlights

- » Environmentally Responsible
- » Roundabout
- » Realignment of Woodbourne Road
- » Auxiliary Turn Lanes
- » Pedestrian Enhancements
- » Bicycle Enhancements
- » Storm Water Management

Design Milestones

- » Scoping Field View Meeting August 2017
- » Archaeological Resources Posting October 2018
- » Scoping Approval March 2019
- » Historic Resources Posting May 2019
- » Safety Review Approval September 2019
- » Design Field View Submission January 2020
- » Section 4(f) Document approved March 2020
- » Section 6(f) Document Submitted May 2020.

Anticipated Schedule

- » Environmental Clearance and Right-of-Way Plan Approval ~6 months
- » Final Design, Right-of-Way Acquisition, NPDES Permit, Utility Coordination/Clearance~18 months
- » Project Advertisement, Letting, NTP ~4 months
- » Construction ~15 months.

Township Responsibilities

- » Engineering
- » Park Replacement Lands
- » Traffic Signals
- » Maintenance Agreement (TBD)

Wrap-up

- » Cooperative Project: Middletown Township, Bucks County, BCCD, Neshaminy School District, PennDOT District 6-0, PennDOT Central Office, FHWA, PADEP, PADCNR, PHMC, PAFBC, FHWA, U.S. Park Service.
- » Questions?
